

Bonita Unified School District

Center for Performing Arts

Construction Progress Report

March 11, 2013





Schedule Status

| | |
|-----------------------|--------------------|
| Construction Duration | 570 days* |
| Time Elapsed | 172 days* |
| Time Remaining | 398 days* |
| Start Date | September 20, 2012 |
| Completion Date | April 13, 2014 |


*Days are calendar days

Completed Activities

- Stage walls up to final height of 54'-10"
- Auditorium walls up to final height of 54'-10"
- Elevator tower to 16'
- Auditorium underground duct work
- Multi-Purpose Room masonry to 16'



Electric and Multi-Purpose Rooms (foreground). Stage and Auditorium (background).

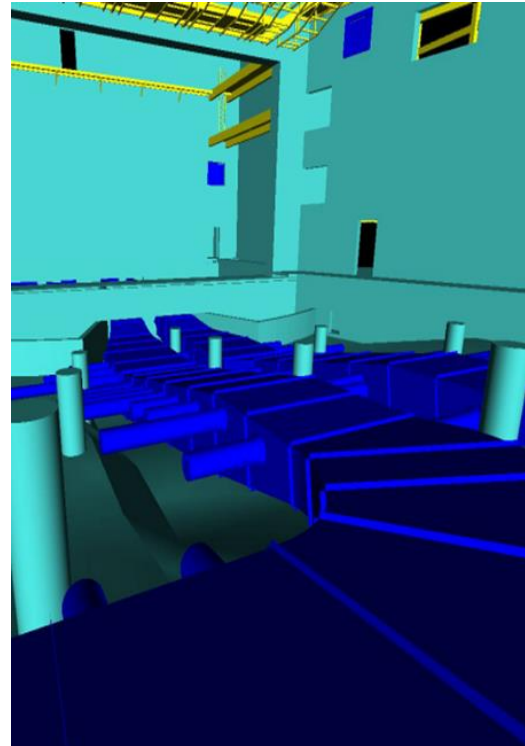

HVAC duct under future audience seating.



Interior of stage looking toward audience.



Bonita Unified School District Center for Performing Arts
Construction Progress Report
March 11, 2013



Elevator tower and auditorium. Elevator tower forms in foreground.



Upcoming Activities

Concrete – Installation of shoring for the audience seating elevated slab has started and will be poured in early April.

Masonry Walls – Masonry walls for back-of-house (B.O.H.) and multi-purpose room are in progress. Masonry walls for the circular restroom will begin by March 25th. All masonry will be complete by April 26th.


Structural Steel – Installation of the balcony steel is scheduled to begin on March 18th, followed by the lobby and auditorium roof steel. Structural steel installation will continue through May.



Shoring for elevated concrete slab for future audience seating. Duct work in foreground.



Bonita Unified School District Center for Performing Arts
Construction Progress Report
March 11, 2013

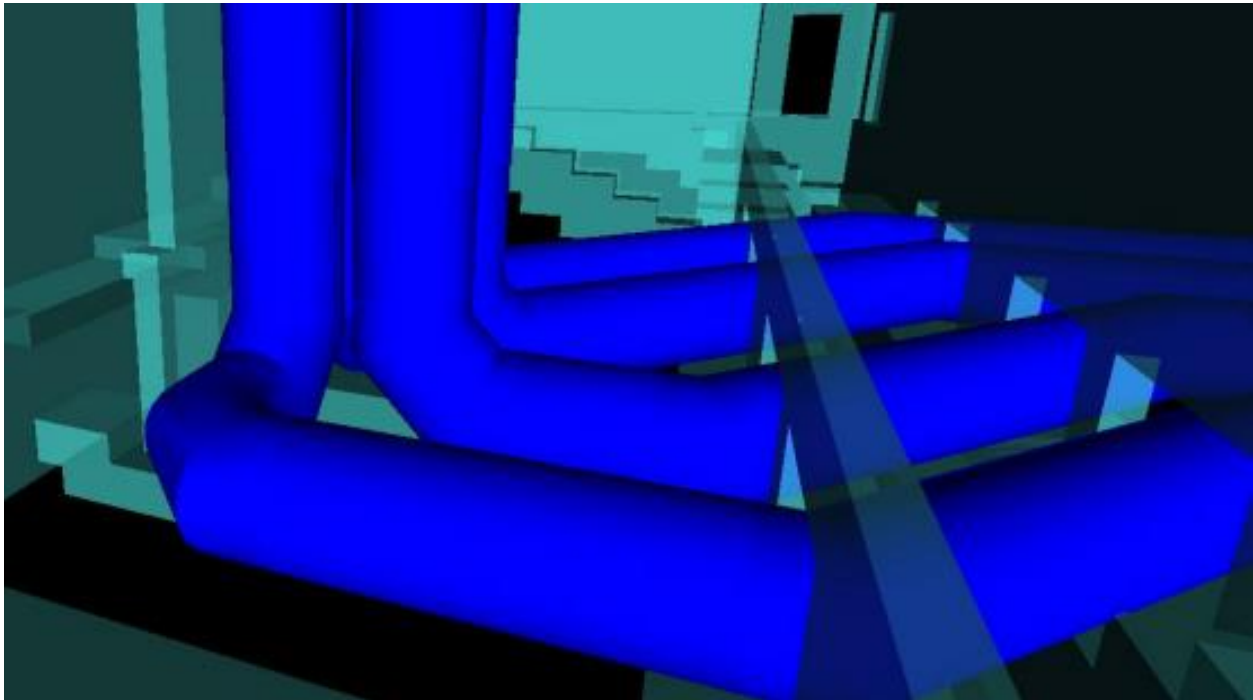

Underground duct to supply audience seating
